

# BLOOMFIELD MAIN STREET REHABILITATION PROJECT




Public Information Centre (PIC) #2

March 23, 2026 @ Bloomfield Town Hall

# PROJECT BACKGROUND

- PEC received \$2,058,969 (90%) in provincial funding through the Ministry of Transportation's Connecting Links Program.
- Approximate project limits from Corey Street to Wellington Street (1.0 km).
- Construction activities are scheduled to commence starting **Monday, March 30<sup>th</sup>**
- Construction is planned to begin at the Intersection of Corey Street and work westerly to the Intersection of Wellington Street.

Construction contract  
awarded to  
**Drew Harrison Haulage  
Ltd.**

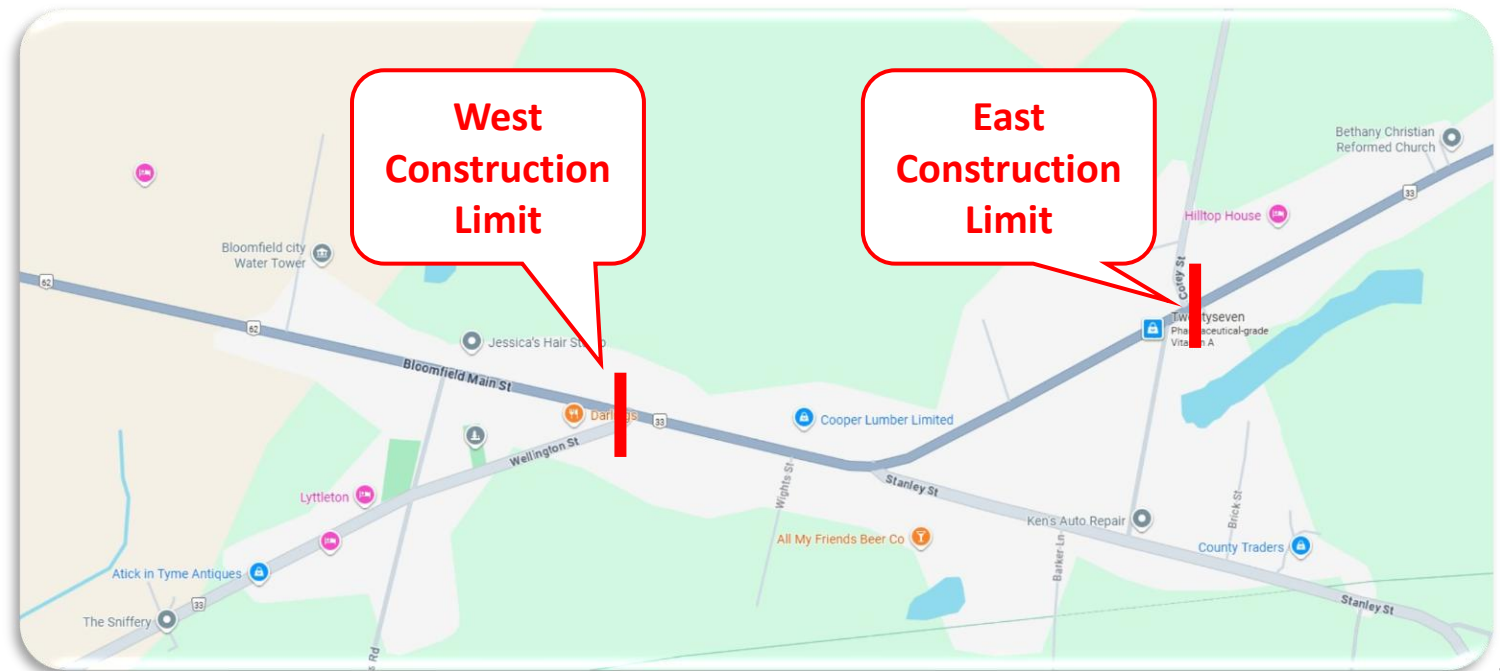


# SCOPE OF WORK

- Select sections of underground storm sewer replacement
- Concrete curb and sidewalk repairs
  - Select sidewalk panels only, no full closure of sidewalk
- Boulevard replacement
  - East of Stanley Street = decorative concrete
  - West of Stanley Street = asphalt
- Roadway asphalt replacement
- Line painting

## Like-for-Like Project

No changes to existing layout of parking, curb, sidewalk or road. Simply repair/replace

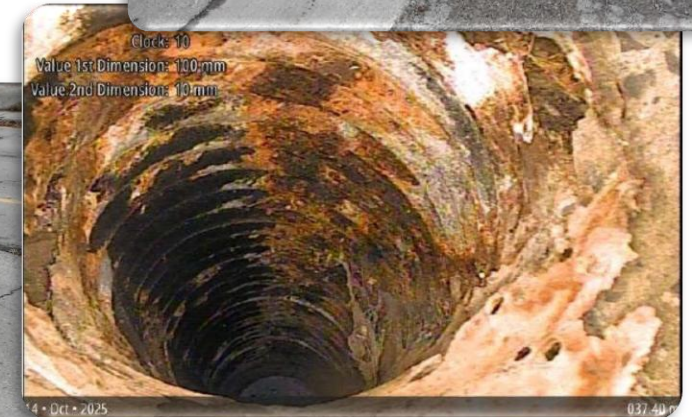

# BUILDING CONDITION SURVEYS



- Contractor will be utilizing the services of **ASC Environmental Inc.** to complete inspection surveys.
- These surveys typically include interior and exterior photographs, to record the visual conditions of existing houses and buildings adjacent to the construction.
- These inspections are done to protect both the municipality and your interests as well as remain confidential.
- Notification and instructions for booking will be sent to residents and businesses beginning March 19<sup>th</sup>.
- You may book your appointment for the pre-construction inspection starting the week of March 23<sup>rd</sup>.
- Questions, concerns, or booking info please contact [info@ascenvironmental.ca](mailto:info@ascenvironmental.ca) or call **(613) 634-5596**.
- A post-construction survey will then be completed once construction is completed.
- This service is free of charge.

# CONSTRUCTION SCHEDULE

## April

Week 1	<ul style="list-style-type: none"> <li>• Float Equipment (mobilization)</li> <li>• Signage, traffic control, locates and pre-construction building surveys</li> <li>• Mark curb and sidewalk for removal</li> <li>• Storm sewer replacement beginning at Corey St</li> </ul>
Week 2	<ul style="list-style-type: none"> <li>• Storm sewer replacement and curb/sidewalk/boulevard removal continues west</li> <li>• New curb/sidewalk/boulevard begins at Corey Street</li> </ul>
Week 3	<ul style="list-style-type: none"> <li>• Storm sewer replacement and curb/sidewalk/boulevard removal continues west</li> <li>• New curb/sidewalk/boulevard continues west</li> </ul>
Week 4	<ul style="list-style-type: none"> <li>• Storm sewer replacement and curb/sidewalk/boulevard removal continues west</li> <li>• New curb/sidewalk/boulevard continues west</li> </ul>

## May

Week 5	<ul style="list-style-type: none"> <li>• Storm sewer replacement and curb/sidewalk/boulevard removal continues west</li> <li>• New curb/sidewalk/boulevard continues west</li> </ul>
Week 6	<ul style="list-style-type: none"> <li>• Full depth asphalt milling begins at Corey Street and continues west</li> <li>• Fine grade road</li> <li>• New curb/sidewalk/boulevard continues west</li> </ul>
Week 7	<ul style="list-style-type: none"> <li>• New decorative concrete boulevard</li> <li>• Pave base course asphalt</li> <li>• Temporary line painting</li> <li>• Adjust manhole lids</li> </ul>
Week 8	<ul style="list-style-type: none"> <li>• Adjust manhole lids</li> <li>• Pave top course asphalt</li> <li>• Permanent line painting</li> </ul>

## June

Week 9	<ul style="list-style-type: none"> <li>• Miscellaneous asphalt repairs (driveways and boulevards)</li> <li>• Miscellaneous line painting</li> </ul>
Week 10	<ul style="list-style-type: none"> <li>• Post-construction building surveys</li> <li>• Remove signage, traffic control and equipment (demobilization)</li> </ul>
Week 11	<ul style="list-style-type: none"> <li>• No planned work</li> </ul>
Week 12	<ul style="list-style-type: none"> <li>• No planned work</li> </ul>

# LOCAL SIGNAGE & PARKING PLAN



- Daily single lane closures in active work area only, using portable traffic lights
- Two-way traffic to resume at the end of each working day

**P**

Public parking remains available at the public parking lot at 289 Main St (Town Hall) & the public lot adjacent to Corey St intersection

**P**

Public parking will also be made available at the Emmanuel Baptist Church

# MUNICIPAL SERVICES



## Emergency Services

- Emergency access for Paramedics, Police and Fire Services, shall be accommodated and available at all times.

## Bus Service

- Both school and County Transit buses shall continue to operate as normal.
- Any changes to route or pick-up/drop-off locations shall be communicated to the public.



## Garbage and Recycling Collection

- PEC (contracted to Environmental 360 Solutions) will continue to collect garbage, compost and recycling on the usual day of the week.
- Where necessary, the contractor will bring waste bins to a designated location for collection and return the empty bins to the appropriate address each week.
- It is advised to label your bins with your address to ensure proper return.



# EXPECTED IMPACTS TO RESIDENTS & BUSINESS



## Hours of Work

- Work will take place Monday to Friday from 7am to 7pm
- All construction related noise must comply with PEC Noise By-Law 143-2022.

## Driveway Access


- The Contractor will notify and coordinate with business owners of any temporary restrictions to driveway access in advance of any disruptions.



## Vibration and Dust

- Vibrations may be experienced during construction.
- Due to vibration, it is encouraged to monitor objects on shelves for buildings located close to the roadway.
- The Contractor will take the necessary steps to reduce dust caused by the construction, ie: concrete wetting and watering of temporary gravel roadways.

# COMMUNICATIONS



- The County will frequently issue Public Service Announcements (PSAs) to provide project updates
- Each Friday update to be issued with what got done and what to expect next
- PSAs are posted on the County website and social media channels
- Please sign up to receive PSA notices and news directly from the County to your email, by visiting <https://www.thecounty.ca/newsletter-signup/>



- The consulting firm (Jewell Engineering Inc.) assisting the County with this project will have a full-time Site Inspector present on site for the duration of construction. The County Project Manager shall also be on site part-time.
- Notices with contact details for project team members have been hand delivered to each resident within the construction zone.
- Businesses/ residents with questions may:
  - ➔ 1. speak directly with the PEC/Jewell On-Site Inspector
  - ➔ 2. contact a project team member from the hand delivered notice
  - ➔ 3. contact the municipality general phone/email

# FEEDBACK & COMMENTS

- You may contact either of the project team members listed below at any time should you have any additional questions or would like to provide feedback.
- Please provide your feedback to help us deliver this project in the least disruptive way possible:
  - ➔ **1. Complete a comment sheet (leave it with us or email it to us)**
  - ➔ **2. Email your comments directly to either of the staff members listed below**
- The County is hosting a virtual Public Information Centre (PIC) on **March 26, 2026, starting at 6pm.**
- Same information as today to be presented. Link to join virtual meeting below.

<https://events.teams.microsoft.com/event/efe2c0c0-1d43-4254-8234-a56967619da8@495d6caf-2637-4a6f-887b-50b7ef293293>



**County of Prince Edward**  
Garrett Osborne, C.E.T., PMP  
Project Manager, Development Services  
613-476-2148 x 2002  
gosborne@pecounty.on.ca



**Jewell Engineering Inc.**  
Pat Schick, A.Sc.T  
Project Manager, Jewell  
613-969-1111  
pat@jewelleng.ca
